



**Monitoring report form
(Version 05.1)**

Complete this form in accordance with the Attachment "Instructions for filling out the monitoring report form" at the end of this form.

MONITORING REPORT

Title of the project activity	Wind Power Project in Tinwari, Rajasthan	
UNFCCC reference number of the project activity	6160	
Version number of the monitoring report	01	
Completion date of the monitoring report	19/08/2017	
Monitoring period number and duration of this monitoring period	02 (01/03/2013 to 31/07/2017; Inclusive of first & last dates of Monitoring Period)	
Project participant(s)	Wind World (India) Limited ¹ (India) ACT Commodities B.V. (Netherland)	
Host Party	India	
Sectoral scope(s)	Sectoral Scope: 1, Energy industries (renewable / non-renewable sources)	
Selected methodology(ies)	ACM0002, version 12.2.0 ("Grid-connected electricity generation from renewable sources")	
Selected standardized baseline(s)	NA	
Estimated amount of GHG emission reductions or net GHG removals by sinks for this monitoring period in the registered PDD	143,336 ² tonnes of CO _{2e}	
Total amount of GHG emission reductions or net GHG removals by sinks achieved in this monitoring period	GHG emission reductions or net GHG removals by sinks reported up to 31 December 2012	GHG emission reductions or net GHG removals by sinks reported from 1 January 2013 onwards
	NA	126,148 tonnes of CO _{2e}

¹ Previous name "Enercon (India) Limited".

² Refer Section E.6 for calculation of estimated amount of GHG emission reduction for this monitoring period in the registered PDD.

SECTION A. Description of project activity

A.1. Purpose and general description of project activity

>>

Wind world (India) Limited (hereafter referred as "WWIL") has developed 20MW wind power project at Jodhpur district of Rajasthan, India. The purpose of the project activity is to harness energy from the renewable source "wind" and generate clean electricity by utilizing Wind Energy Converters (WECs) throughout the project lifetime. In the absence of the project activity equivalent amount of electricity would have been generated from the existing connected/ new power plants in the NEWNE grid, which are predominantly based on fossil fuels. Whereas the operation of Wind Energy Convertors (WEC's) is emission free and no emissions occur during the lifetime of the project activity.

Brief description of the installed technology and equipments:

The Project activity is consist of 25 WECs of Enercon make E-53³ type WECs of 800kW capacity each aggregating to the capacity of 20.0 MW. The WECs generates 3-phase power at 400V, which is stepped up to 33 kV and further transmitted to WWIL Sub-station. From WWIL substation electricity is further evacuated to the Rajasthan regional electricity grid which is part of the NEWNE (Northern, Eastern, Western and North-Eastern) grid in India. The clean and green electricity supplied by the project will aide in sustainable growth in the region. Wind world (India) Limited⁴ is the project owner and project participant for the project activity.

Wind World (India) Ltd has established a manufacturing plant at Daman in India, where along with other components the "Synchronous Generators" using "Vacuum Impregnation" technology are manufactured.



Technology Diagram

Relevant dates for the project activity:

The first machine under the project activity was commissioned on 30/09/2011 and last machine under the project activity was commissioned on 09/11/2011. Project activity has got registered under CDM on 25/07/2012 & fixed crediting period started from 01/08/2012. The expected operational lifetime of the project is for 20 years. Details of previous verification period & issuance are as follows:

Issuance no.	Period covered	CER issued	
First Issuance	01/08/2012 to 28/02/2013 (Inclusive of both days)	12,777	(8258 from CP1)

The total emission reductions achieved under current monitoring period (01/03/2013 to 31/07/2017; Inclusive of both dates) are 126,148 tCO_{2e}.

³ Technology details has been provided in Appendix-2 of the MR

⁴ Previous name - Enercon (India) Limited

A.2. Location of project activity

>>

- a. Host Party(ies) : India
- b. Region/State/Province, etc : Rajasthan State
- c. City/Town/Community, etc : Salodi, Chensingh Nagar, Bari, Malunga, Bada Kotacha, Digadi Dhani, Balrva & Beru villages of Jodhpur district
- d. Physical / Geographical location : A location map is provided in Appendix 3. The detailed individual WECs location numbers and coordinates of project activity are provided below:

S.No.	WEC Loc No.	Village	Latitude (N)	Longitude (E)
1	9	SALODI	26.42828	72.80512
2	48	Chain singh Nagar/Balrva	26.45382	72.87220
3	49	Chain singh Nagar/Balrva	26.45383	72.86990
4	50	Chain singh Nagar/Balrva	26.45661	72.87060
5	51	Chain singh Nagar/Balrva	26.45580	72.86707
6	53	Chain singh Nagar/Balrva	26.45745	72.86628
7	82	Bari	26.47798	72.83214
8	83	Bari	26.47596	72.82855
9	112	Malunga	26.45374	72.77689
10	113	Malunga	26.45609	72.77677
11	114	Malunga	26.45756	72.77531
12	115	Malunga	26.46012	72.77523
13	116	Malunga	26.45891	72.77188
14	129	Digadi Dhani (Malunga)	26.49696	72.79726
15	130	Bada Kotacha	26.50309	72.80070
16	131	Bada Kotacha	26.50395	72.79868
17	133	Bada Kotacha	26.50955	72.79788
18	134	Bada Kotacha	26.51170	72.79732
19	136	Digadi Dhani (Malunga)	26.50604	72.79201
20	137	Digadi Dhani (Malunga)	26.50539	72.79512
21	501	Chain singh Nagar/Balrva	26.45836	72.86488
22	504	Beru	26.42481	72.87424
23	515	Digadi Dhani (Malunga)	26.50039	72.79619
24	516	Digadi Dhani (Malunga)	26.50245	72.79325
25	517	Digadi Dhani (Malunga)	26.50828	72.79092

A.3. Parties and project participant(s)

Party involved ((host) indicates a host Party)	Private and/or public entity(ies) project participants (as applicable)	Indicate whether the Party involved wishes to be considered as project participant (yes/no)
India (host)	Wind World (India) Limited (Private entity)	No
Netherland	ACT Commodities B.V. (Private entity)	No

A.4. Reference of applied methodology and standardized baseline

>>

Title: Consolidated baseline and monitoring methodology for “Grid-connected electricity generation from renewable sources”

Reference: Approved consolidated baseline methodology ACM0002 (Version 12.2.0, EB 58)

UNFCCC web reference of methodology:
<http://cdm.unfccc.int/methodologies/PAmethodologies/approved.html>

ACM0002 draws upon the following tools which have been used in the PDD:

- Tool to calculate the emission factor for an electricity system – Version 02.2.1⁵
- Tool for the demonstration and assessment of additionality – Version 05.2⁶

A.5. Crediting period of project activity

>>

Type of crediting period	:	Fixed
Start date of crediting period	:	01/08/2012
Length of crediting period	:	10 years

A.6. Contact information of responsible persons/entities

>>

Wind World (India) Limited
 A-9, Veera Industrial Estate, Veera Desai Road, Andheri West
 Mumbai, Maharashtra 400 053 (India)

The detailed contact information has been provided in Appendix 1. The above mentioned person/entity is also a project participant.

⁵ <http://cdm.unfccc.int/methodologies/PAmethodologies/tools/am-tool-07-v2.2.1.pdf>

⁶ <http://cdm.unfccc.int/methodologies/PAmethodologies/tools/am-tool-01-v5.2.pdf>

SECTION B. Implementation of project activity

B.1. Description of implemented registered project activity

>>

The project activity consists of 25 machines (800 kW each) of Enercon make E-53. The commissioning dates for all the machines include in the project activity are given in the table below:-

S.No.	WEC Loc No.	Village	Date of Commissioning
1	9	Salodi	30 Sep 2011
2	48	Chain singh Nagar/Balrva	09 Nov 2011
3	49	Chain singh Nagar/Balrva	09 Nov 2011
4	50	Chain singh Nagar/Balrva	09 Nov 2011
5	51	Chain singh Nagar/Balrva	09 Nov 2011
6	53	Chain singh Nagar/Balrva	09 Nov 2011
7	82	Bari	30 Sep 2011
8	83	Bari	30 Sep 2011
9	112	Malunga	09 Nov 2011
10	113	Malunga	09 Nov 2011
11	114	Malunga	09 Nov 2011
12	115	Malunga	09 Nov 2011
13	116	Malunga	09 Nov 2011
14	129	Digadi Dhani (Malunga)	30 Sep 2011
15	130	Bada Kotacha	30 Sep 2011
16	131	Bada Kotacha	30 Sep 2011
17	133	Bada Kotacha	30 Sep 2011
18	134	Bada Kotacha	30 Sep 2011
19	136	Digadi Dhani (Malunga)	30 Sep 2011
20	137	Digadi Dhani (Malunga)	30 Sep 2011
21	501	Chain singh Nagar/Balrva	09 Nov 2011
22	504	Beru	09 Nov 2011
23	515	Digadi Dhani (Malunga)	30 Sep 2011
24	516	Digadi Dhani (Malunga)	30 Sep 2011
25	517	Digadi Dhani (Malunga)	30 Sep 2011

Wind world (India) Limited operation and maintenance activities are ISO 9001:2008 certified. Referring to the data available it can be inferred that there have not been any major special events for any of the machines that are included in the project activity. As a part of regular maintenance the machines are stopped for mechanical and electrical maintenance for few hours annually and for visual inspection for 6 to 7 hours quarterly. Furthermore, the consolidated performance report of project WECs during the monitoring period including the down time, machine availability, grid availability, etc. has been provided in Appendix 5. During the monitoring period there were no events or situations occurred, which may impact the applicability of the methodology.

The WECs generates 3-phase power at 400V, which is stepped up to 33 kV and electricity transmitted to WWIL Sub-station. At WWIL sub-station electricity is step-up to 132 kV. From Wind World substation metering point electricity is further evacuated to the state electricity grid at 132kV. The Project can operate in the frequency range of 47.5–51.5 Hz and in the voltage range of 400 V \pm 12.5%. The other salient features of the state-of-art-technology are:-

- Gearless Construction - Rotor & Generator Mounted on same shaft eliminating the Gearbox.
- Variable Pitch functions ensuring maximum energy capture.
- Near Unity Power Factor at all times.
- Minimum drawal (less than 1% of kWh generated) of Reactive Power from the grid.

- No voltage peaks at any time.
- Operating range of the WEC with voltage fluctuation of -20 to +20%.
- Less Wear & Tear since the system eliminates mechanical brake, which are not needed due to low speed generator which runs at maximum speed of 32 rpm and uses Air Brakes.
- Three Independent Braking Systems.
- Generator achieving rated output at only 32 rpm.
- Incorporates lightning protection system, which includes blades.
- Starts generation of power at wind speed of 3 m/s

B.2. Post-registration changes

B.2.1. Temporary deviations from registered monitoring plan, applied methodology or applied standardized baseline

>>

Not applicable

B.2.2. Corrections

>>

Not applicable

B.2.3. Changes to start date of crediting period

>>

Not applicable

B.2.4. Inclusion of a monitoring plan to the registered PDD that was not included at registration

>>

Not applicable

B.2.5. Permanent changes from registered monitoring plan, applied methodology or applied standardized baseline

>>

Not applicable

B.2.6. Changes to project design of registered project activity

>>

Not applicable

B.2.7. Types of changes specific to afforestation or reforestation project activity

>>

Not applicable

SECTION C. Description of monitoring system

>>

Wind World (India) Limited is O&M contractor for the project activity and will be responsible for the maintaining all the monitoring data in respect of the project activity. Wind World (India) Limited has implemented the management structure for managing the monitored data.

This approved monitoring methodology requires monitoring of the following:


- Net electricity supplied from the project activity;

Emission factor of NEWNE electricity grid of the project activity is fixed ex-ante hence no further monitoring of this parameter is required. As per ACM0002 leakage need not be considered hence leakage has not been considered for the project activity. Hence, the sole parameter for monitoring is the net electricity supplied by the project activity to the grid.

The Project activity is operated and managed by the Wind World (India) Limited. The operational and maintenance activity is taken care by the service department of Wind World, which is an ISO 9001 certified company. Wind World follows the documentation practices to ensure the reliability and availability of the data for all the activities as required from the identification of the site, wind resource assessment, logistics, finance, construction, commissioning and operation of the wind power project.

Calculation of Net Electricity Supplied to the grid by project activity:

Layout of Metering arrangement for project activity is as follows:-

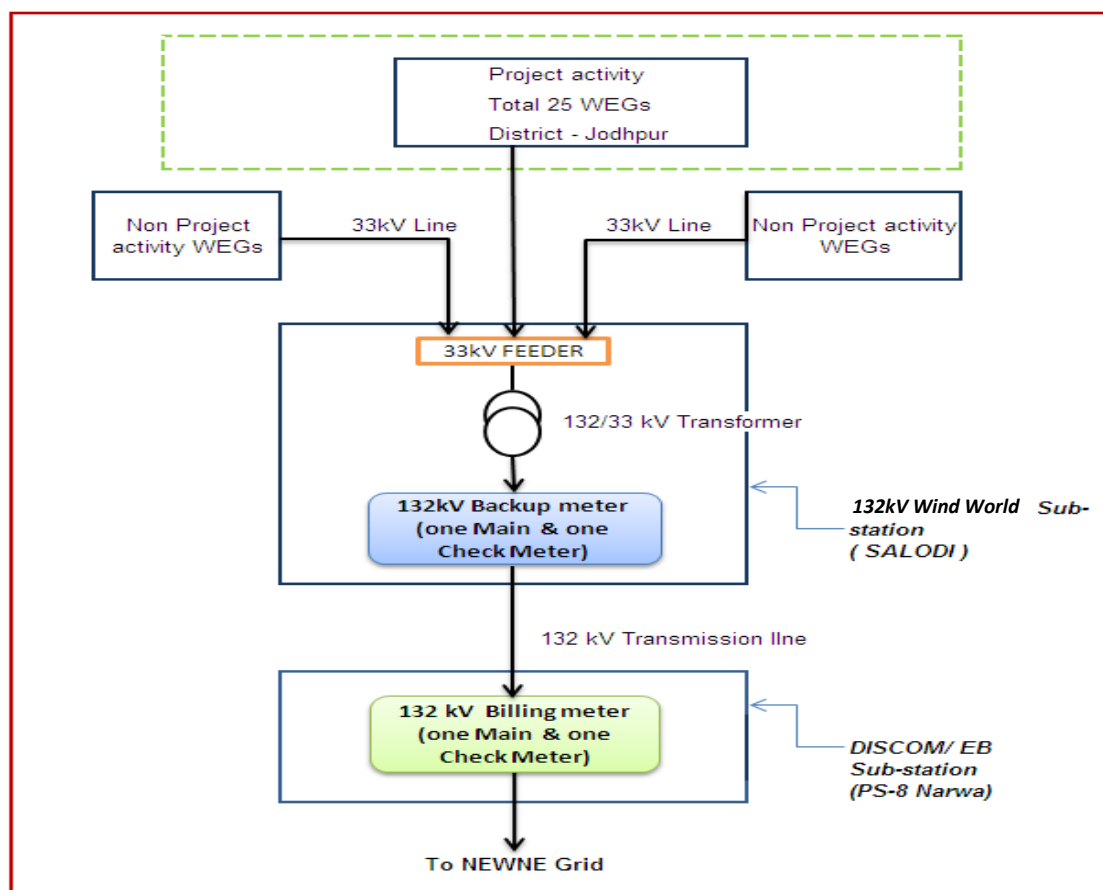

From the above layout it is clear that project activity WECs (25Nos) along with WECs of other customers, who are not the part of project activity are connected to Wind World Sub-stations which are further connected to EB sub-station through EHV line. The 25WECs of project activity installed in Jodhpur district is

connected through 132kV Wind World (India) Limited pooling sub-station (132kV SALODI sub-station), through 33kV feeder lines. At Wind World pooling sub-station SALODI electricity is stepped up to 132kV, wherein the backup meter (one main & one check meter) connected. From Wind World pooling sub-station electricity is transmitted to state utility (DISCOM) sub-station (PS-8 Narwa Sub-station) through 132kV transmission line/ EHV line wherein billing meter (one main & one check meter) is connected. At EB sub-station metering is done at 132kV billing meter. From state utility sub-station electricity is further transmitted to NEWNE grid.

The net electricity supplied to the grid will be calculated on monthly basis at the EB/DISCOM substations (PS-8 Narwa) wherein the billing meter is connected. The monthly joint meter readings are taken by the representatives of DISCOM and WWIL (PP's representative) who also signs the JMR. Simultaneously, the monthly joint meter reading of backup meters available at WWIL pooling sub-station (SALODI) is also taken by representatives of RVPN/DISCOM and WWIL. The copy of JMR at backup meters is available with Wind World.

Since, the project activity WECs are connected through common metering system along with non-project activity WECs of other customers at the main meter, apportioning of electricity export & import as recorded in JMR is being done to calculate the electricity export & import by individual WECs/ customers. Apportioning is being done based on the net electricity generation (Gross Export – Gross Import) recorded at LCS meter installed in individual WECs

Based on the monthly JMR reading, which is signed by representative of DISCOM and PP's representative (WWIL); WWIL prepares the monthly breakup generation sheets which indicate export, import & the net electricity supplied by individual customers to the grid. An apportioning procedure is used by PP's representative to arrive at net electricity supplied to the grid by individual investors.

The monthly generation sheet is submitted to both, DISCOM as well as individual investors. PP raises the invoice based on the monthly breakup sheet corresponding to the net electricity generation value indicated in the monthly breakup sheet. DISCOM based on the JMR reading along with monthly breakup sheet prepared by WWIL and the invoice raised, conduct the audit to cross check the net electricity values and in case all the values are found to be correct, DISCOM release the payment against the invoice raised by individual investors.

The values of the net electricity supplied to grid by project activity can be cross checked with invoices raised by the PP on DISCOM and/or RTGS transaction or cheque copy.

Procedure for apportioning:-

Procedure used by PP's representative to prepare monthly breakup sheets for project activity:-

The monthly JMR reading contains the electricity export, import & net electricity supplied by all the WECs of project activity as well as non-project activity connected to the metering system at DISCOM substation. Hence in order to arrive at the electricity export, import & net electricity supplied by WECs of the project activity based on the net electricity generation (Gross Export – Gross Import) recorded at LCS meter, following procedure is used by O&M contractor (WWIL):-

Net electricity generation (Gross Export – Gross Import) by WECs of project activity,

$$\sum \mathbf{EG}_{\text{Controller, } j} = \sum_{j=1}^n \mathbf{EG}_{\text{Controller, } j}$$

Where, **n** is the number of WECs ($n = 1$ to 25) in project activity.

Net electricity generation (Gross Export – Gross Import) by all WECs (Project activity & non project activity) connected to Discom substation,

$$\sum \mathbf{EG}_{\text{Controller, } i} = \sum_{i=1}^{j+k} \mathbf{EG}_{\text{Controller, } i}$$

Where, $j+k$ is the number of WECs (project activity & non-project activity) connected to sub-station.

As LCS meter measures the net electricity generation (Gross Export – Gross Import) by individual WEC, which is the difference of export and import and doesn't provide individual reading of Export & Import; the apportioning of electricity export & import at recorded at billing meter as indicated in JMR sheet is done

based on net electricity generation (Gross Export – Gross Import) of WECs. This is a standard procedure that is followed in the state of Rajasthan and is accepted by the state DISCOM for payment of tariff invoices.

Electricity exported by all WECs of project activity is apportioned on the basis of summation of net electricity generation (Gross Export – Gross Import)⁷ (by all the WECs (j number of WECs) of project activity, as measured at the controller (LCS meter) at project site and the electricity export recorded at the main meter mentioned in the JMR. The formula used for computing electricity export to the grid by the project activity is as follows:-

Electricity Export to the grid by the Project activity,

$$EG_{\text{Export},y} = \frac{EG_{\text{JMR,Export}} * \sum EG_{\text{Controller},j}}{\sum EG_{\text{Controller},i}} \dots\dots\dots(1)$$

As LCS meter measures the net electricity generation (Gross Export – Gross Import) by WECs and doesn't provide individual reading of Export & Import. Therefore apportioning of export as well as import for all WEC of the project activity is also apportioned on the basis of summation of net electricity generation (Gross Export – Gross Import) by all the WECs (j number of WECs) of project activity, as measured at the controller (LCS meter) at project site and the electricity import recorded at the main meter mentioned in the JMR. The formula used for computing electricity import from the grid by the project activity is as follows

Electricity Import from the grid by the Project activity,

$$EG_{\text{Import},y} = \frac{EG_{\text{JMR,Import}} * \sum EG_{\text{Controller},j}}{\sum EG_{\text{Controller},i}} \dots\dots\dots(2)$$

Wherein,

$\sum EG_{\text{Controller},j}$ = Summation of net electricity generation (Gross Export – Gross Import) by all the WECs (j number of WECs) of project activity, as measured at the controller (LCS meter) at project site

$\sum EG_{\text{Controller},i}$ = Summation of net electricity generation (Gross Export – Gross Import) by all WEC (i number of WECs) of project activity or non-project activity, as measured at the controller (LCS meter) at project site

$EG_{\text{JMR,Export}}$ = Electricity export by project and non-project recorded at respective billing meters located at DISCOM sub-station. This can be checked from JMR certificates.

$EG_{\text{JMR,Import}}$ = Electricity import by project and non-project recorded at respective billing meters located at DISCOM sub-station. This can be checked from JMR certificates.

$EG_{\text{Export},y}$ = Electricity export by project activity calculated as per formula 1 above

$EG_{\text{Import},y}$ = Electricity import by project activity calculated as per formula 2 above.

Therefore net electricity supplied to grid by 25 WECs of the project activity is calculated as the difference of equation (1) & (2),

$$EG_{\text{Facility},y} = EG_{\text{Export},y} - EG_{\text{Import},y}$$

⁷ LCS meter installed in individual WEGs control panel measures the net/ gross electricity generation (Export- Import) by WEG and therefore $\sum EG_{\text{Controller},j}$ is used by developer to calculate electricity export & import by individual developer (project activity & non project activity WEGs)..

⁸ The report detailing the value of $\sum EG_{\text{Controller}}$ can be provided to the verifying DOE on request.

Even though the above mentioned of apportioning is done by the PP's representative and submitted to respective DISCOM, the same undergoes the series of audit by the hierarchy of auditors (Asst. Auditors, divisional auditors & account auditors) and then finally authorised by the Superintending engineer (SE) of the circle office of respective DISCOMs.

The above method of apportioning is not conducted by the PP but is described in details only to provide the clear description of entire procedure by relevant authority

Procedure to deal with data uncertainty:


During the annual calibration, if the meter is found to be outside the permissible limits of the error and if that meter readings have been used in JMR, the (–ve) error value would be applied to electricity export and (+ve) error value will be applied to import of electricity from grid to all the JMR values since the date of last calibration. The meter would be replaced immediately with new calibrated meter.

Training and maintenance requirements:

Training on the machine is an essential pre-requisite, to ensure necessary safety of man and machine. Further, in order to maximize the output from the Wind Energy Converters (WECs), it is extremely essential, that the engineers and technicians understand the machines and keep them in good health. In order to ensure, that Enercon's service staffs is deft at handling technical snags on top of the turbine, the necessity of ensuring that they are capable of climbing the tower with absolute ease and comfort has been established. The Enercon Training Academy provides need-based training to meet the training requirements of Enercon projects. The training is contemporary, which results in imparting focused knowledge leading to value addition to the attitude and skills of all trainees. This ultimately leads to creativity in problem solving.

Monitoring roles and responsibilities

The operational and management structure implemented for data monitoring is as follows:

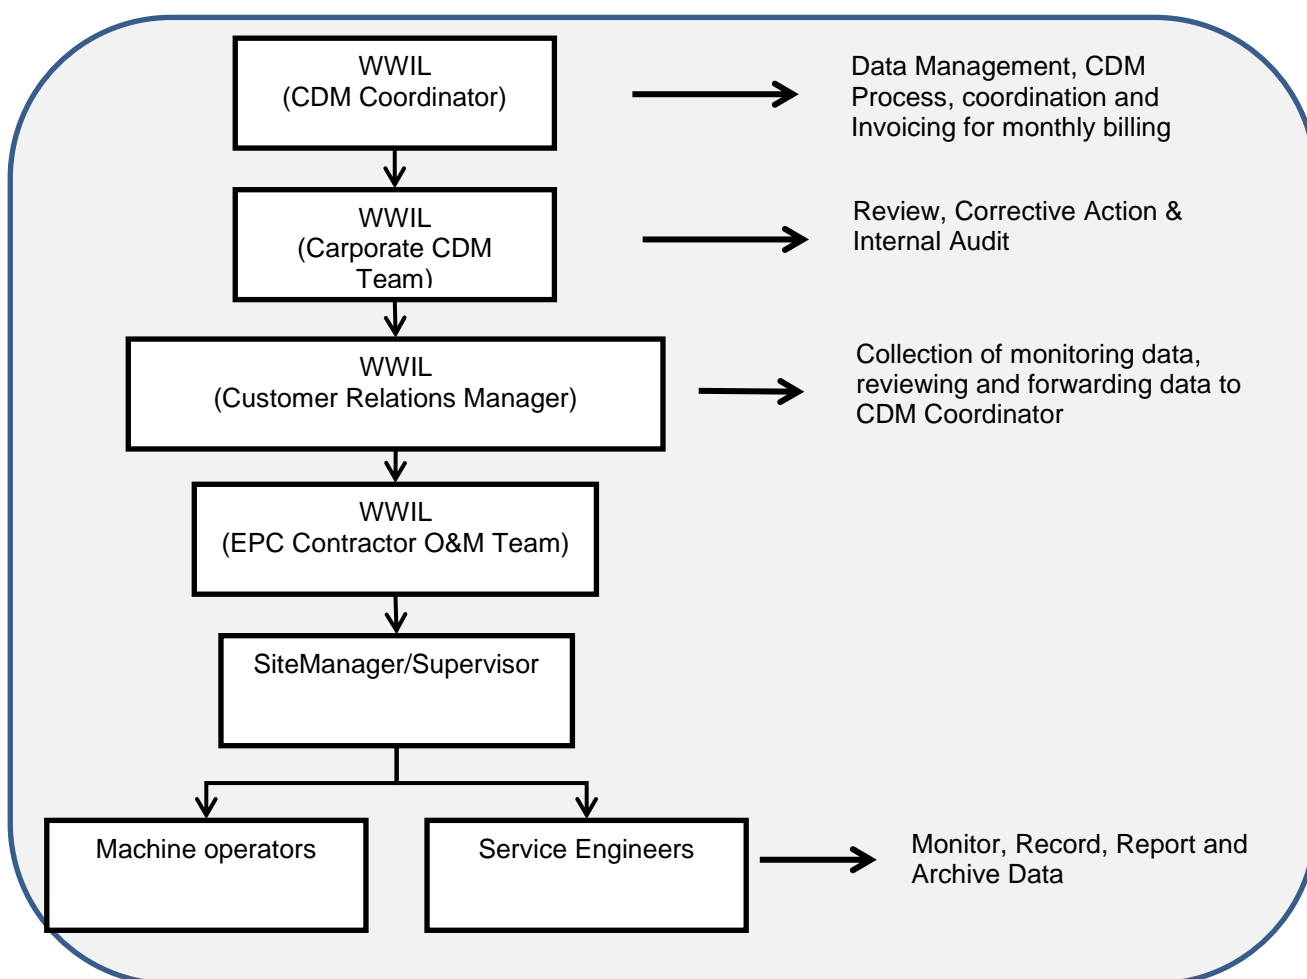

Meter Test Checking Details:

The metering equipment were inspected & tested by State Utility. Meter details & calibration details for the all the main and check meters are as follows:-

Location of meter		PS-8 Sub-station (Electricity Board) (Billing metering point)		Salodi Sub-station (Enercon) (Back metering point)	
Type of meter		Main Meter	Check Meter	Main meter	Check Meter
Meter Sr. No.		RJB 00354	RJB 00356	RJB 00358	RJB 00357
Meter Make		Secure	Secure	Secure	Secure
Accuracy class		0.20%	0.20%	0.20%	0.20%
Type		All the meters are two-way Tri-vector meters capable of recording import and export of electricity.			
Calibration Dates					
	2012	20-Dec-12	20-Dec-12	20-Dec-12	20-Dec-12
Due Date of calibration		20-Dec-13	20-Dec-13	20-Dec-13	20-Dec-13
	2014	11-Mar-14	11-Mar-14	11-Mar-14	11-Mar-14
Due Date of calibration		11-Mar-15	11-Mar-15	11-Mar-15	11-Mar-15
	2015	21-Feb-15	21-Feb-15	21-Feb-15	21-Feb-15
Due Date of calibration		21-Feb-16	21-Feb-16	21-Feb-16	21-Feb-16
	2016	11-Feb-16	11-Feb-16	11-Feb-16	11-Feb-16
Due Date of calibration		11-Feb-17	11-Feb-17	11-Feb-17	11-Feb-17
	2017	01-Feb-17	01-Feb-17	01-Feb-17	01-Feb-17
Due Date of calibration		01-Feb-18	01-Feb-18	01-Feb-18	01-Feb-18

The main and check meters are tested for accuracy on annual basis by state utility and in case of error; meters are calibrated by state utility. Further during the annual meter testing, all the meters were under the permissible limit of error and accordingly none of the meter was replaced during the current monitoring period. However, delay in calibration has been observed in the year 2013. Therefore, as per guideline EB 52 Annex 60 para 4a & 5, PP has applied maximum permissible error for all measured values taken during the period between the scheduled date of calibration and the actual date of calibration conservatively. Please refer Sheet "ER calculation sheet" for detailed calculation.

SECTION D. Data and parameters

D.1. Data and parameters fixed ex ante or at renewal of crediting period

Data / Parameter:	$EF_{CM,y}$		
Unit:	tCO _{2e} /MWh		
Description:	Combined Margin Emission Factor of NEWNE Electricity Grid		
Source of data:	<p>Combined Margin Emission Factor ($EF_{grid,CM,y}$) is calculated as the weighted average of Operating Margin Emission Factor ($EF_{grid,OM,y}$) and Build Margin Emission Factor ($EF_{grid,BM,y}$).</p> <p>The “CO₂ Baseline Database for Indian Power Sector”, version 6.0, published by the Central Electricity Authority, Ministry of Power, Government of India.</p> <p>The “CO₂ Baseline Database for Indian Power Sector” is available at http://www.cea.nic.in/reports/planning/cdm_co2/cdm_co2.htm</p>		
Value(s) applied:	<p>“CO₂ Baseline Database for Indian Power Sector”, version 6.0 published by the Central Electricity Authority, Ministry of Power, Government of India.</p> <table border="1"> <tr> <td>Combined Margin Emission Factor ($EF_{grid,CM,y}$)</td><td>0.94881</td></tr> </table> <p>Refer Appendix 4 for comprehensive calculation of Combined Margin Emission Factor.</p>	Combined Margin Emission Factor ($EF_{grid,CM,y}$)	0.94881
Combined Margin Emission Factor ($EF_{grid,CM,y}$)	0.94881		
Purpose of data:	Calculation of Baseline Emissions		
Additional comment:	This value is calculated on ex-ante basis and will remain fixed for the entire crediting period.		

Data / Parameter:	$EF_{OM,y}$
Unit:	tCO _{2e} /MWh
Description:	Operating Margin Emission Factor of NEWNE Electricity Grid
Source of data:	<p>“CO₂ Baseline Database for Indian Power Sector”, version 6.0, published by the Central Electricity Authority, Ministry of Power, Government of India.</p> <p>The “CO₂ Baseline Database for Indian Power Sector” is available at http://www.cea.nic.in/reports/planning/cdm_co2/cdm_co2.htm</p>
Value(s) applied:	0.99431
Purpose of data:	Calculation of Baseline Emissions
Additional comment:	This value is calculated on ex-ante basis and will remain fixed for the entire crediting period.

Data / Parameter:	$EF_{BM,y}$
Unit:	tCO _{2e} /MWh
Description:	Build Margin Emission Factor of NEWNE Electricity Grid
Source of data:	<p>“CO₂ Baseline Database for Indian Power Sector”, version 6.0, published by the Central Electricity Authority, Ministry of Power, Government of India.</p> <p>The “CO₂ Baseline Database for Indian Power Sector” is available at http://www.cea.nic.in/reports/planning/cdm_co2/cdm_co2.htm</p>

Value(s) applied:	0.81231
Purpose of data:	Calculation of Baseline Emissions
Additional comment:	This value is calculated on ex-ante basis and will remain fixed for the entire crediting period.

D.2. Data and parameters monitored

Data / Parameter:	EG_{facility,y}
Unit:	MWh (Mega-watt hour)
Description:	Net electricity generation supplied to the grid by the Project activity.
Measured/ Calculated / Default:	Calculated
Source of data:	Generation break-up sheets prepared by the developer (WWIL), which is based on monthly JMR reading recorded at main meter installed at DISCOM sub-station and the LCS controller meter (panel meter) reading.
Value(s) of monitored parameter:	132,954.656
Monitoring equipment:	Since, it is calculated value, hence not applicable.
Measuring/ Reading/ Recording frequency:	Frequency of recording data: Monthly Refer section 'C' (Description of monitoring system) for an illustration of the provisions for measurement methods.
Calculation method (if applicable):	The procedures for calculation of net electricity supplied to grid has been followed as per the provisions of the power purchase agreement and details of calculation method has been explained in monitoring plan under section C of monitoring report.
QA/QC procedures:	Value of EG _{facility,y} can be cross checked with the tariff invoices raised on the DISCOM and/or RTGS transaction or cheque copy. All the billing (Main & Check) & Backup (Main & Check) meters are calibrated by DISCOM annually and the records are available with the representative of PP (WWIL)
Purpose of data:	Calculation of Baseline Emissions
Additional comment:	The data will be archived both in electronic and hard paper format for crediting period + 2 years.

Data / Parameter:	EG_{Export,y}
Unit:	MWh (Mega-watt hour)
Description:	Electricity export to the grid by the Project activity.
Measured/ Calculated / Default:	Measured
Source of data:	Generation break-up sheets prepared by the developer (WWIL), which is based on monthly joint meter reading recorded at main meter installed at DISCOM sub-station and the LCS controller meter (panel meter) reading.
Value(s) of monitored parameter:	133,132.295
Monitoring equipment:	Please refer section 'C' (Description of monitoring system) for the details of meter type, accuracy class, serial number, meter test checking frequency, date of last meter test checking and validity under the heading 'Meter Test Checking Details'

Measuring/ Reading/ Recording frequency:	Frequency of recording data: Monthly. Further all the meters have the capability of continuous measurement of data. Refer section 'C' for an illustration of the provisions for measurement methods.
Calculation method (if applicable):	-
QA/QC procedures:	Value of $EG_{Export,y}$ can be cross checked with the tariff invoices raised on the DISCOM and/or RTGS transaction or cheque copy. All the billing & Back meters are calibrated by DISCOM annually and the records are available with the representative of PP (WWIL)
Purpose of data:	Calculation of Baseline Emissions
Additional comment:	The data will be archived both in electronic and hard paper format for crediting period + 2 years.

Data / Parameter:	$EG_{Import,y}$
Unit:	MWh (Mega-watt hour)
Description:	Electricity Import from grid by the Project activity.
Measured/ Calculated / Default:	Measured
Source of data:	Generation break-up sheets prepared by the developer (WWIL), which is based on monthly meter reading recorded at main meter installed at DISCOM sub-station and the LCS controller meter (panel meter) reading.
Value(s) of monitored parameter:	177.639
Monitoring equipment:	Please refer section 'C' (Description of monitoring system) for the details of meter type, accuracy class, serial number, meter test checking frequency, date of last meter test checking and validity under the heading 'Meter Test Checking Details'
Measuring/ Reading/ Recording frequency:	Frequency of recording data: Monthly Further all the meters have the capability of continuous measurement of data. Refer section 'C' for an illustration of the provisions for measurement methods.
Calculation method (if applicable):	-
QA/QC procedures:	Value of $EG_{Import,y}$ can be cross checked with the tariff invoices raised on the DISCOM and/or RTGS transaction or cheque copy. All the billing & Back meters are calibrated by DISCOM annually and the records are available with the representative of PP (WWIL).
Purpose of data:	Calculation of Baseline Emissions
Additional comment:	The data will be archived both in electronic and hard paper format for crediting period + 2 years

Data / Parameter:	$EG_{JMR, Export}$
Unit:	MWh (Mega-watt hour)
Description:	Electricity export by project activity & non-project activity recorded by main meter installed at DISCOM sub-station.

Measured/ Calculated / Default:	Measured
Source of data:	Monthly JMR sheets recorded by representative of both DISCOM & WWIL
Value(s) of monitored parameter:	616662.364
Monitoring equipment:	Please refer section 'C' (Description of monitoring system) for the details of meter type, accuracy class, serial number, meter test checking frequency, date of last meter test checking and validity under the heading 'Meter Test Checking Details'
Measuring/ Reading/ Recording frequency:	Frequency of recording data: Monthly Further all the meters have the capability of continuous measurement of data. Refer section 'C' for an illustration of the provisions for measurement methods.
Calculation method (if applicable):	-
QA/QC procedures:	All the billing & Backup meters are calibrated by DISCOM annually and the records are available with the representative of PP (WWIL)
Purpose of data:	Calculation of Baseline Emissions
Additional comment:	The data will be archived both in electronic and hard paper format for crediting period + 2 years

Data / Parameter:	EG_{JMR, Import}
Unit:	MWh (Mega-watt hour)
Description:	Electricity import by project activity & non project activity recorded by main meter installed at DISCOM sub-station
Measured/ Calculated / Default:	Measured
Source of data:	Monthly JMR sheets recorded by representative of both DISCOM & WWIL.
Value(s) of monitored parameter:	816.583
Monitoring equipment:	Please refer section 'C' (Description of monitoring system) for the details of meter type, accuracy class, serial number, meter test checking frequency, date of last meter test checking and validity under the heading 'Meter Test Checking Details'
Measuring/ Reading/ Recording frequency:	Frequency of recording data: Monthly Further all the meters have the capability of continuous measurement of data. Refer section 'C' for an illustration of the provisions for measurement methods.
Calculation method (if applicable):	-
QA/QC procedures:	All the billing & Backup meters are calibrated by DISCOM annually and the records are available with the representative of PP (WWIL).
Purpose of data:	Calculation of Baseline Emissions
Additional comment:	The data will be archived both in electronic and hard paper format for crediting period + 2 years

Data / Parameter:	EG_{Controller, i}
Unit:	MWh (Mega-watt hour)
Description:	<p>Net electricity generation (Gross Export – Gross Import) by a WEC of project activity or non-project activity, as measured at the controller (LCS meter) at project site. Each WEC has exclusive LCS meter that records net electricity generation (Gross Export – Gross Import) from the WEC (project or non-project).</p> <p>Where,</p> <p>i is any WEC between 1 to j+ k.</p> <p>j is number of WEC of project activity connected to main meter at DISCOM substation and backup meter at WWIL substation.</p> <p>k is number of WEC of non-project activity connected to main meter at DISCOM substation and backup meter at WWIL substation.</p>
Measured/ Calculated / Default:	Measured
Source of data:	Monthly controller generation report (LCS) sourced from SCADA system installed at project site.
Value(s) of monitored parameter:	Please refer CER calculation sheet for the values of parameter.
Monitoring equipment:	Please refer section 'C' for details of controller meter (LCS).
Measuring/ Reading/ Recording frequency:	<p>Frequency of recording data: Monthly</p> <p>Further all the meters have the capability of continuous measurement of data.</p> <p>Refer section 'C' for an illustration of the provisions for measurement methods.</p>
Calculation method (if applicable):	-
QA/QC procedures:	All the LCS meters are auto calibrated. In case of any fault WEC stops automatically and meter is replaced immediately.
Purpose of data:	Calculation of Baseline Emissions
Additional comment:	The data will be archived in electronic form for crediting period + 2 years.

Data / Parameter:	$\sum EG_{Controller, i}$
Unit:	MWh (Mega-watt hour)

Description	<p>Summation of net electricity generation (Gross Export-Gross Import) by all WEC (i number of WECs) of project activity (j number of WECs) and non-project activity (k number of WECs), as measured at the controller (LCS meter) at project site. Each WEC has exclusive LCS meter that records net electricity generation (Gross Export-Gross Import) from the WEC (project or non-project).</p> <p>Where,</p> <p>i is any WEC between 1 to j+ k and connected to main meter (JMR/billing meter) at DISCOM substation and backup meter at Enercon substation.</p> <p>j is number of WECs of project activity connected to main meter (JMR/billing meter) at DISCOM substation and backup meter at Enercon substation.</p> <p>k is number of WEC of non-project activity connected to main meter (JMR/billing meter) at DISCOM substation and backup meter at Enercon substation.</p>
Measured/ Calculated / Default:	Calculated
Source of data:	Monthly controller generation report (LCS) sourced from SCADA system installed at project site.
Value(s) of monitored parameter:	Please refer CER calculation sheet.
Monitoring equipment:	Please refer section 'C' for details of controller meter (LCS).
Measuring/ Reading/ Recording frequency:	<p>Frequency of recording data: Monthly</p> <p>Further all the meters have the capability of continuous measurement of data.</p> <p>Refer section 'C' for an illustration of the provisions for measurement methods.</p>
Calculation method (if applicable):	Please refer section 'C' for calculation procedure.
QA/QC procedures:	All the LCS meters are auto calibrated. In case of any fault WEC stops automatically and meter is replaced immediately.
Purpose of data:	Calculation of Baseline Emissions
Additional comment:	The data will be archived in electronic form for crediting period + 2 years.

Data / Parameter:	$\sum EG_{\text{Controller}, j}$
Unit:	MWh (Mega-watt hour)
Description:	<p>Summation of net electricity generation (Gross Export – Gross Import) by all the WECs (j number of WECs) of project activity, as measured at the controller (LCS meter) at project site. Each WEC has exclusive LCS meter that records net electricity generation (Gross Export – Gross Import) from the WEC (project or non -project).</p> <p>j is number of WEC of project activity connected to main meter at DISCOM substation and backup meter at WWIL substation.</p>
Measured/ Calculated / Default:	Calculated
Source of data:	Monthly controller generation report (LCS) sourced from SCADA system installed at project site.

Value(s) of monitored parameter:	Please refer CER calculation sheet.
Monitoring equipment:	Please refer section 'C' for details of controller meter (LCS).
Measuring/ Reading/ Recording frequency:	Frequency of recording data: Monthly Further all the meters have the capability of continuous measurement of data. Refer section 'C' for an illustration of the provisions for measurement methods.
Calculation method (if applicable):	Please refer section 'C' for calculation procedure.
QA/QC procedures:	All the LCS meters are auto calibrated. In case of any fault WEC stops automatically and meter is replaced immediately.
Purpose of data:	Calculation of Baseline Emissions
Additional comment:	The data will be archived in electronic form for crediting period + 2 years.

D.3. Implementation of sampling plan

>>

Not Applicable.

SECTION E. Calculation of emission reductions or GHG removals by sinks

E.1. Calculation of baseline emissions or baseline net GHG removals by sinks

>>

"The baseline is the quantity of electricity (MWh) produced by the renewable generating unit multiplied by an emission coefficient (measured in t CO₂e/MWh) calculated in a transparent and conservative manner as the weighted average emissions (in t CO₂e/MWh) as described in registered PDD.

$$BE_y = EG_{PJ,y} * EF_{grid, CM, y}$$

Where:

BE_y = Baseline emissions in year y (tCO₂/yr)
 $EG_{PJ,y}$ = Quantity of net electricity generation that is produced and fed into the grid as a result of the implementation of the CDM project activity in year y (MWh/yr)
 $EF_{grid, CM, y}$ = Combined margin CO₂ emission factor for grid connected power generation in year y calculated using the latest version of the "Tool to calculate the emission factor for an electricity system" (tCO₂/MWh)

Baseline emission factor (Combined Margin) ($EF_{grid, CM, y}$) = 0.94881 tCO₂e/MWh.

Since, the project activity is the installation of a new grid connected renewable power plant the $EG_{PJ,y}$ is calculated as :

$$EG_{PJ,y} = EG_{facility,y}$$

$EG_{facility,y}$ = Quantity of net electricity generation supplied by the project plant/unit to the grid in year y (MWh/yr)

Baseline Emission Reductions calculation for project activity:-

Duration	Electricity export to the grid by the Project activity [MWh]	Electricity import from grid by the Project activity [MWh]	Net electricity generation supplied to the grid by the Project activity [MWh]	Baseline Emission Factor (tCO ₂ e/MWh)	Baseline Emissions (tCO ₂ e)
	[$EG_{Export,y}$]	[$EG_{Import,y}$]	[$EG_{facility,y}$]	[EF_y]	[BE_v] = [$EG_{facility,y}$] * [EF_v]
01/03/2013 to 31/07/2017	133,132.295	177.639	132,954.656	0.94881	126,148

E.2. Calculation of project emissions or actual net GHG removals by sinks

>>

Since the project activity is a renewable energy project which generates electricity using wind power and hence does not result in project emissions.

E.3. Calculation of leakage

>>

No leakage is considered from the project activity as per approved methodology ACM0002.

E.4. Summary of calculation of emission reductions or net GHG removals by sinks

Item	Baseline emissions or baseline net GHG removals by sinks (t CO ₂ e)	Project emissions or actual net GHG removals by sinks (t CO ₂ e)	Leakage (t CO ₂ e)	GHG emission reductions or net GHG removals by sinks (t CO ₂ e) achieved in the monitoring period		
				Up to 31/12/2012	From 01/01/2013	Total amount
Total	126,148	0	0	0	126,148	126,148

E.5. Comparison of actual emission reductions or net GHG removals by sinks with estimates in registered PDD

Item	Values estimated in ex ante calculation of registered PDD	Actual values achieved during this monitoring period
Emission reductions or GHG removals by sinks (t CO ₂ e)	143,336 ⁹ (32,415 p.a. emission reductions estimated in the registered PDD has been extrapolated for the current monitoring period i.e. for 1614 days)	126,148

E.6. Remarks on difference from estimated value in registered PDD

>>

This monitoring period (01/03/2013 to 31/07/2017) covers 53 months i.e. 1614 days and the actual emission reductions achieved for this monitoring period are 126,148 tCO_{2e}. Since, the registered PDD estimated emission reduction annually, therefore emission reductions estimated in the registered PDD (i.e. 32,415tCO_{2e}/annum) has been extrapolated for the current monitoring period i.e. for 1614 days and the extrapolated emission reduction are 143336¹⁰ tCO_{2e}. There is marginal change of 11.99% (downside) in the expected and annual emission reductions since the monitoring period include the low wind season leading to low plant load factor during the monitoring period.

⁹ Detailed Calculation is provided in ER sheet.

¹⁰ Detailed Calculation is provided in ER sheet.

Appendix 1. Contact information of project participants and responsible persons/entities

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Person/entity responsible for completing the CDM-MR-FORM
Organization name	Wind World (India) Limited
Street/P.O. Box	A-9, Veera Industrial Estate, Veera Desai Road, Andheri (W)
Building	Wind World Tower
City	Mumbai
State/region	Maharashtra
Postcode	400053
Country	India
Telephone	+91-22-6692 4848
Fax	+91-22 - 67040473 / 66921175
E-mail	Yogeshh.mehra@windworldindia.com
Website	http://www.windworldindia.com/index.jsp
Contact person	
Title	Managing Director
Salutation	Mr.
Last name	Mehra
Middle name	
First name	Yogeshh
Department	Corporate
Mobile	+91-98200 40301
Direct fax	+91-22-6692 1177
Direct tel.	+91-22-6702 2832
Personal e-mail	Yogeshh.mehra@windworldindia.com

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Person/entity responsible for completing the CDM-MR-FORM
Organization name	ACT Commodities B.V.
Street/P.O. Box	Gustav Mahlerlaan
Building	1082 MK
City	Amsterdam
State/region	
Postcode	1009
Country	Netherlands
Telephone	+31-2089 11 250
Fax	+31-2089 11 787
E-mail	wkuipers@group-act.com
Website	
Contact person	
Title	Authorised Signatory
Salutation	Mr.
Last name	Bastiaansen
Middle name	
First name	Bram
Department	
Mobile	
Direct fax	+31-2089 11 787
Direct tel.	+31-2089 11 780
Personal e-mail	wkuipers@group-act.com



Appendix-2

WECs Technology employed in the project activity:

Turbine model	Enercon E- 53
Rated power	800 KW
Rotor diameter	53 m
Hub height	75 m
Turbine Type	Gearless horizontal axis wind turbine with variable rotor speed
Power regulation	Independent electromechanical pitch system for each blade.
Cut in windspeed	2.5 m/s
Rated wind speed	12 m/s
Cut out Windspeed	28-34 m/s
Extreme Wind Speed	59.5 m/s
Rated rotational speed	32 rpm
Operating range rot. speed	12-29 rpm
Orientation	Upwind
No of Blades	3
Blade Material	Glass Fiber reinforced Epoxy
Gear box type	Gear less
Generator type	Synchronous generator
Braking	Aerodynamic
Output Voltage	400 V
Yaw System	Active yawing with 4 electric yaw drives with brake motor and friction bearing
Tower	74 m concrete

Appendix-3

Project Geographical Location:

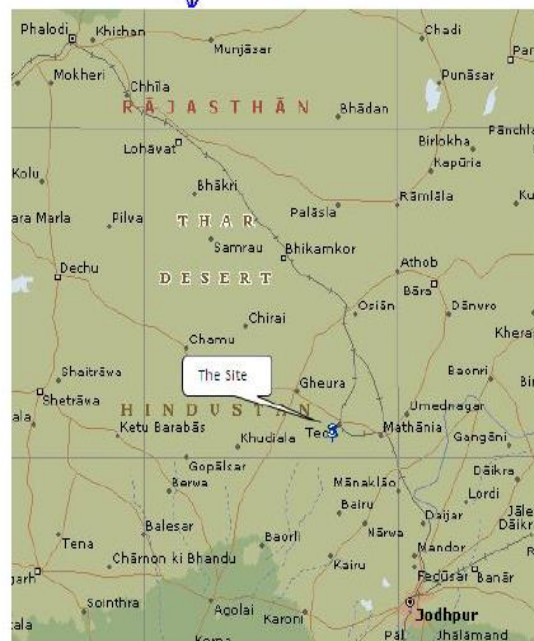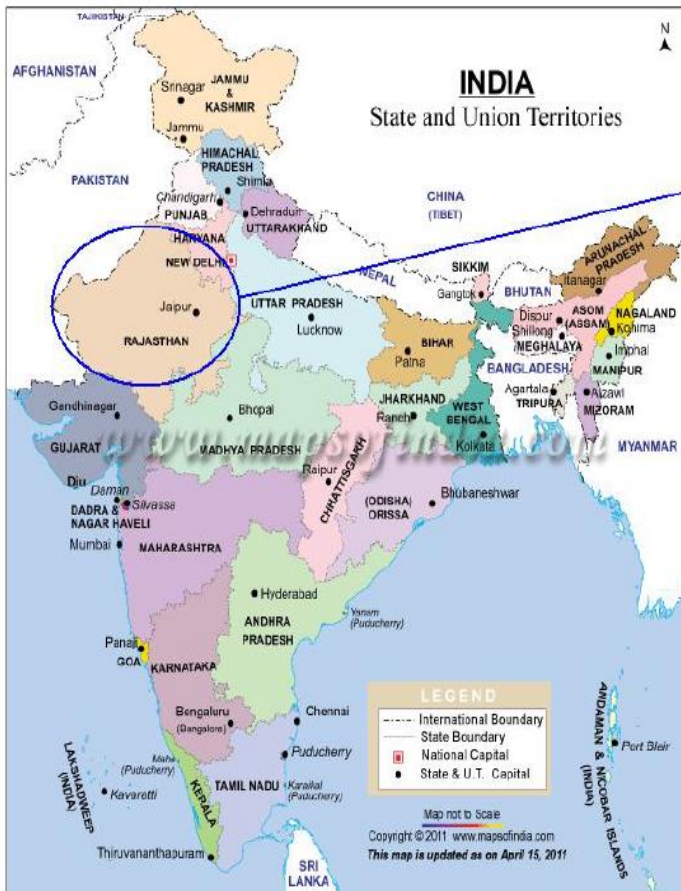

Appendix-4

BASELINE INFORMATION

The Operating Margin data for the most recent three years and the Build Margin data for the NEWNE Grid as published in the "CO₂ Baseline Database for Indian Power Sector"¹¹, Version 6.0, 1st March, 2011, published by Central Electricity Authority (CEA), Government of India have been used for the estimation of the Baseline Emission. The Operating Margin data for the most recent three years and the Build Margin data for the NEWNE are as follows:

Simple Operating Margin

	NEWNE Grid (tCO ₂ e/GWh)	Net Generation Total (MWh)
Simple Operating Margin – 2007-08	0.99990	496.119
Simple Operating Margin – 2008-09	1.00655	510.693
Simple Operating Margin – 2009-10	0.97774	544.915
Weighted Average Operating Margin *		0.99431

* Calculated as per Option A, i.e. generation weighted average CO₂ emissions per unit electricity generation has been used

Build Margin

	NEWNE Grid (tCO ₂ e/GWh)
Build Margin- 2009-10	0.81231

Combined Margin Calculations

	Weights	NEWNE Grid (tCO ₂ e/GWh)
Operating Margin	0.75	0.99431
Build Margin	0.25	0.81231
Combined Margin		0.94881

Detailed information on calculation of Operating Margin Emission Factor and Build Margin Emission Factor is available at www.cea.nic.in.

¹¹ http://www.cea.nic.in/reports/planning/cdm_co2/cdm_co2.htm

Appendix-5

WECs Performance Report

State	RAJASTHAN	Monthly Performance Report					Date:01/03/2013-31/07/2017		
WEC No.	Lack Of Wind	Down Time					Machine Availability(%)	Capacity Factor (%)	Grid Availability(%)
		Machine		Grid		Total			
		Fault	Shutdown	Fault	Shutdown				
Site: TINWARI,RAJASTHAN	WIND WORLD (WINDFARMS) INDIA LTD							Total WEC : 25	
EILTI-01 (130)	3984:39:00	882:05:00	137:24:00	483:58:00	204:17:00	6218:10:00	97.31	16.35	97.73
EILTI-02 (131)	3525:36:00	1142:47:00	140:38:00	484:23:00	204:47:00	6151:08:00	96.62	18.52	97.73
EILTI-03 (515)	3800:03:00	890:17:00	135:02:00	488:41:00	202:28:00	6045:49:00	97.3	15.34	97.73
EILTI-04 (129)	3578:03:00	911:40:00	133:54:00	476:35:00	199:12:00	5777:45:00	97.25	17.69	97.77
EILTI-05 (516)	3782:36:00	622:04:00	133:44:00	476:25:00	202:25:00	5695:35:00	98.01	16.93	97.76
EILTI-06 (137)	3817:50:00	781:48:00	131:15:00	486:19:00	204:02:00	6163:48:00	97.6	15.97	97.73
EILTI-07 (133)	3618:56:00	802:44:00	122:02:00	486:56:00	200:46:00	5787:00:00	97.56	17.32	97.74
EILTI-08 (134)	3995:30:00	385:50:00	132:26:00	482:57:00	205:08:00	6066:44:00	98.64	16.11	97.73
EILTI-09 (136)	3503:06:00	2779:04:00	135:05:00	464:44:00	202:22:00	8525:22:00	92.32	15.4	97.79
EILTI-10 (517)	3700:22:00	1369:27:00	132:21:00	488:31:00	202:46:00	7058:17:00	96.04	15.43	97.72
EILTI-11 (82)	4108:33:00	373:45:00	140:40:00	134:08:00	169:04:00	5388:41:00	98.65	17.31	98.75
EILTI-12 (83)	4140:32:00	363:54:00	139:23:00	134:08:00	167:55:00	5390:35:00	98.68	18.1	98.75
EILTI-13 (9)	4009:44:00	720:00:00	121:47:00	272:17:00	177:13:00	6193:35:00	97.78	16.85	98.36
EILTI-14 (112)	3606:33:00	1558:23:00	137:04:00	276:43:00	176:34:00	7369:23:00	95.53	16.69	98.4
EILTI-15 (113)	3842:08:00	1626:41:00	123:23:00	260:30:00	176:01:00	6392:54:00	95.39	17.51	98.39
EILTI-16 (114)	2773:03:00	9817:07:00	90:36:00	275:57:00	176:21:00	13828:38	73.92	14.52	98.36
EILTI-17 (115)	2816:45:00	9180:02:00	107:29:00	275:57:00	174:59:00	13945:54	75.55	11.82	98.35
EILTI-18 (116)	3531:23:00	453:24:00	118:47:00	276:27:00	167:09:00	4888:31:00	98.49	18.81	98.37
EILTI-19 (504)	3840:51:00	409:50:00	135:07:00	302:23:00	208:02:00	6090:12:00	98.56	18.16	98.34
EILTI-20 (48)	3938:10:00	472:55:00	122:20:00	330:30:00	208:00:00	5317:27:00	98.43	18.1	98.28
EILTI-21 (49)	3786:40:00	715:30:00	130:30:00	328:50:00	206:33:00	5413:35:00	97.77	20.95	98.29

EILTI-22 (50)	3528:23:00	1012:52:00	129:25:00	328:54:00	200:55:00	5470:01:00	96.99	21.92	98.3
EILTI-23 (51)	2537:43:00	9308:00:00	116:46:00	299:26:00	201:12:00	13405:55	75.18	17.38	98.38
EILTI-24 (53)	3569:00:00	1175:57:00	154:43:00	325:05:00	202:41:00	5662:58:00	96.49	23.59	98.31
EILTI-25 (501)	3488:12:00	3633:48:00	145:39:00	301:06:00	196:21:00	8420:18:00	90.04	19.58	98.39
Total	90824:21	51389:54	3247:30:00	8941:50:00	4837:13:00	176668:15	94.24	17.45	98.14

- - - -

Document information

<i>Version</i>	<i>Date</i>	<i>Description</i>
05.1	4 May 2015	Editorial revision to correct version numbering.
05.0	1 April 2015	Revisions to: <ul style="list-style-type: none"> • Include provisions related to delayed submission of a monitoring plan; • Provisions related to the Host Party; • Remove reference to programme of activities; • Overall editorial improvement.
04.0	25 June 2014	Revisions to: <ul style="list-style-type: none"> • Include the Attachment: Instructions for filling out the monitoring report form (these instructions supersede the "Guideline: Completing the monitoring report form" (Version 04.0)); • Include provisions related to standardized baselines; • Add contact information on a responsible person(s)/ entity(ies) for completing the CDM-MR-FORM in A.6 and Appendix 1; • Change the reference number from <i>F-CDM-MR</i> to <i>CDM-MR-FORM</i>; • Editorial improvement.
03.2	5 November 2013	Editorial revision to correct table in page 1.
03.1	2 January 2013	Editorial revision to correct table in section E.5.

<i>Version</i>	<i>Date</i>	<i>Description</i>
03.0	3 December 2012	Revision required to introduce a provision on reporting actual emission reductions or net GHG removals by sinks for the period up to 31 December 2012 and the period from 1 January 2013 onwards (EB70, Annex 11).
02.0	13 March 2012	Revision required to ensure consistency with the "Guidelines for completing the monitoring report form" (EB 66, Annex 20).
01	28 May 2010	EB 54, Annex 34. Initial adoption.
Decision Class: Regulatory Document Type: Form Business Function: Issuance Keywords: monitoring report		
