



**Monitoring report form**  
**(Version 04.0)**

*Complete this form in accordance with the Attachment "Instructions for filling out the monitoring report form" at the end of this form.*

**MONITORING REPORT**

<b>Title of the project activity</b>	La Venta II
<b>Reference number of the project activity</b>	0846
<b>Version number of the monitoring report</b>	1
<b>Completion date of the monitoring report</b>	07/08/2014
<b>Registration date of the project activity</b>	25/06/2007
<b>Monitoring period number and duration of this monitoring period</b>	Monitoring Period 6 01/01/2013 – 30/06/2014
<b>Project participant(s)</b>	<p><b>Mexico:</b> Comisión Federal de Electricidad; International Bank for Reconstruction and Development (IBRD) as the Trustee of the Spanish Carbon Fund (SCF)</p> <p><b>Kingdom of Spain:</b> Ministry of Agriculture, Food and Environment and Ministry of Economy and Competitiveness ; AZULIBER 1, S.L. ; Comercial De Materiales De Construcción, S.L. (COMAC) ; Compania Espanola De Petroleos, S.A. (CEPSA) ; Endesa Generacion, S.A. ; E.ON Generacion S.L ; Gas Natural SDG, S.A. ; Hidroelectrica Del Cantabrico, S.A. ; IBERDROLA Generacion S.A.U ; Repsol YPF S.A. ; Zeroemissions Carbon Trust, S.A. ; Cementos Portland Valderrivas S.A. ; International Bank for Reconstruction and Development (IBRD) as Trustee of the Spanish Carbon Fund (SCF)</p>
<b>Host Party(ies)</b>	Mexico
<b>Sectoral scope and selected methodology(ies), and where applicable, applied standardized baseline(s)</b>	<p>1 : Energy industries (renewable - / non- renewable sources)</p> <p>ACM0002 ver. 6 - Consolidated methodology for grid-connected electricity generation from renewable sources</p>
<b>Estimated amount of GHG emission reductions or net anthropogenic GHG removals by sinks for this monitoring period in the registered PDD</b>	289,609 tCO <sub>2</sub> e
<b>Actual GHG emission reductions or net anthropogenic GHG removals by sinks achieved in this monitoring period</b>	175,139 tCO <sub>2</sub> e
<b>Actual GHG emission reductions or net anthropogenic GHG removals by sinks</b>	N/A

achieved during the period up to 31 December 2012 (if applicable)	
Actual GHG emission reductions or net anthropogenic GHG removals by sinks achieved during the period from 1 January 2013 onwards (if applicable).	175,139 tCO <sub>2</sub> e

## SECTION A. Description of project activity

### A.1. Purpose and general description of project activity

The project's purpose is renewable electricity generation to be supplied to the Interconnected Mexican National Grid (IMNG). The project is expected to displace 192,545 tons of carbon dioxide equivalent ("tCO<sub>2</sub>e") per year, which will account to 1,347,815 tCO<sub>2</sub>e for the first crediting period (7 years), generating the equivalent amount of greenhouse gasses emissions reductions ("ERs"). As per the registered PDD, the project's greenhouse gasses (GHG) emissions are negligible, thus there is no need to monitor leakage and it is not taken into account when calculating the ERs.

La Venta II wind power plant (La Venta II) consists of 98 wind turbine-generator engines (WTGs) each of 0.85 MW capacity, adding up to a total installed capacity of 83.3 MW. The WTGs are distributed in 4 rows approximately 600 meters away from each other. The WTGs are approximately 130 meters away from each other; the height of the WTGs is 44 meters. The maximum estimated generation is 307,728 MWh.

The project was fully commissioned on January 5, 2007, and has been in continuous operation since then. Total emission reductions for this monitoring period are **175,139 tCO<sub>2</sub>e**.

### A.2. Location of project activity

- (a) Mexico
- (b) Southern State of Oaxaca
- (c) Ejido La Venta, Juchitan de Zaragoza Municipality
- (d) Latitude 16.59 and Longitude -94.819722

### A.3. Parties and project participant(s)

Party involved ((host) indicates a host Party)	Private and/or public entity(ies) project participants (as applicable)	Indicate if the Party involved wishes to be considered as project participant (Yes/No)
Mexico(host)	Comisión Federal de Electricidad; International Bank for Reconstruction and Development (IBRD) as the Trustee of the Spanish Carbon Fund (SCF)	No

Party involved ((host) indicates a host Party)	Private and/or public entity(ies) project participants (as applicable)	Indicate if the Party involved wishes to be considered as project participant (Yes/No)
Spain	Ministry of Agriculture, Food and Environment and Ministry of Economy and Competitiveness ; AZULIBER 1, S.L. ; Comercial De Materiales De Construccion, S.L. (COMAC) ; Compania Espanola De Petroleos, S.A. (CEPSA) ; Endesa Generacion, S.A. ; E.ON Generacion S.L ; Gas Natural SDG, S.A. ; Hidroelectrica Del Cantabrico, S.A. ; IBERDROLA Generacion S.A.U ; Repsol YPF S.A. ; Zeroemissions Carbon Trust, S.A. ; Cementos Portland Valderrivas S.A. ; International Bank for Reconstruction and Development (IBRD) as Trustee of the Spanish Carbon Fund (SCF)	Yes

#### A.4. Reference of applied methodology and standardized baseline

ACM0002, version 6, Consolidated baseline methodology for grid-connected generation from renewable sources

#### A.5. Crediting period of project activity

Type: Renewable crediting period

Starting date: 01/07/2014

Duration: 7 years 0 months

#### A.6. Contact information of responsible persons/ entities

This monitoring report has been developed by Gaffie Saldivar ([gaffie.saldivar@cfe.gob.mx](mailto:gaffie.saldivar@cfe.gob.mx)) from Comision Federal de Electricidad (Project Participant) in collaboration with Zhuo Cheng ([zcheng@worldbank.org](mailto:zcheng@worldbank.org)) and Patricia Marcos Huidobro ([pmarcoshuidobro@worldbank.org](mailto:pmarcoshuidobro@worldbank.org)) from the International Bank for Reconstruction and Development, as the Trustee of the Spanish Carbon Fund (Project Participant).


## SECTION B. Implementation of project activity

### B.1. Description of implemented registered project activity

#### Implementation Status

La Venta II was commissioned on 5/01/2007, and it has been in continuous operation since then. During this monitoring period La Venta II net generation registered at 34.5 kV was 279,921 MWh. The chart below shows the monthly generation, which varied mainly due to the variability of the wind regimes.

Fig.1. Monthly Electricity Generation

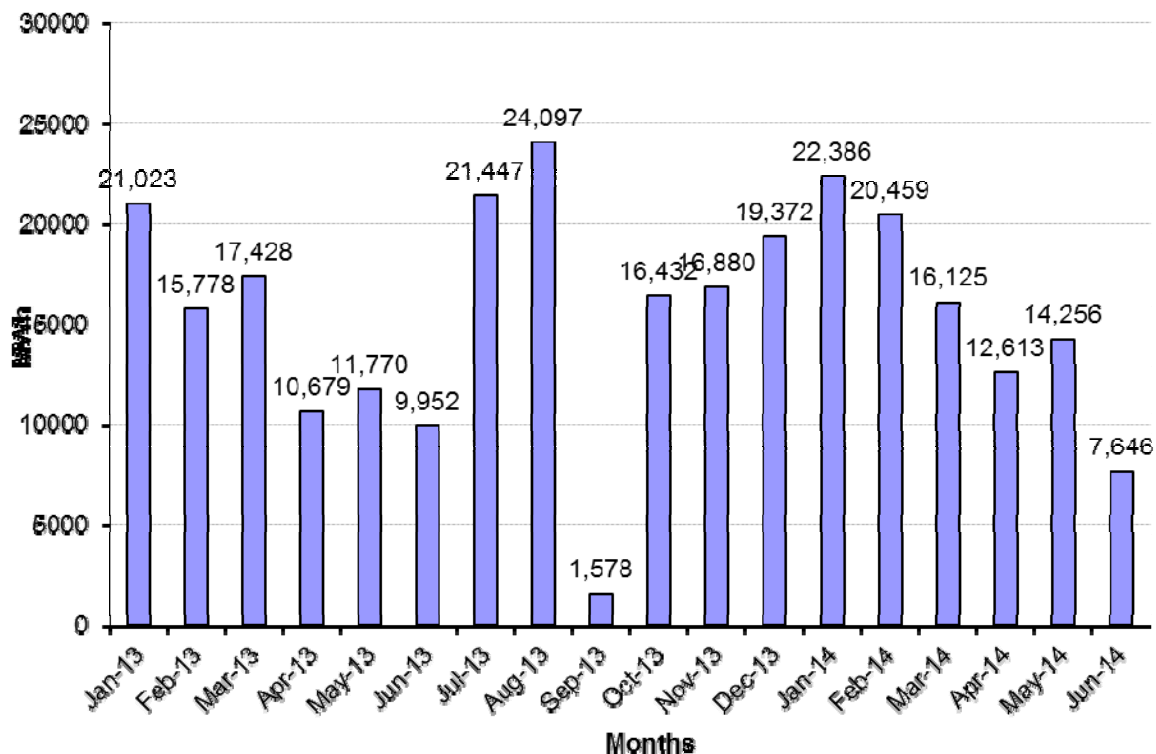

When analyzing the chart above, September 2013, due to the wind conditions outside the operating margin (4 – 25 m/s) there was a low electricity production.

Apart from that, there were no events that occurred during the current monitoring period that would impact the applicability of the methodology.

Of the remaining causes, the two most important are linked to:

- Damage suffered by the components of the wind generators.
- Disconnection from the grid by the system operator (CENACE).

These events lead to an increase in the number of downtime hours. The ER calculations reflect these events.

#### Description of the Installed Technology

La Venta II has a total installed capacity of 83.3 MW and consists of 98 Gamesa G52 wind turbines with 850 kW of rated capacity installed in towers of 44 meters high. Each rotor has a diameter of 52 meters with 3 blades of 25.3 meters long each. The WTGs are distributed in 4 rows about 600 meters away from each other and each WTG is approximately 130 meters away from the adjacent ones.

The cut-in and cut-out wind speeds for these wind turbines are 4 m/s and 25 m/s respectively (for a wind density of 1.225 kg/m<sup>3</sup>). The output voltage of each generator is 690 V. The voltage is increased from 690 V to 34.5 kV through a transformer located in each of the towers of the wind turbines before sending the electricity to the substation. The wind farm is integrated by 5 electric circuits which collect the electricity generated by the 98 WTGs and sends it to La Venta II substation. The total generated electricity is delivered to the grid and commercialized by CFE,

which is the project developer, operator and owner of La Venta II. La Venta II's minimum expected plant operating life is 21 years.

**B.2. Post registration changes****B.2.1. Temporary deviations from registered monitoring plan, applied methodology or applied standardized baseline**

N/A

**B.2.2. Corrections**

N/A

**B.2.3. Permanent changes from registered monitoring plan, applied methodology or applied standardized baseline**

N/A

**B.2.4. Changes to project design of registered project activity**

N/A

**B.2.5. Changes to start date of crediting period**

N/A

**B.2.6. Types of changes specific to afforestation or reforestation project activity**


N/A

**SECTION C. Description of monitoring system**

As per the registered PDD, the only parameter to be monitored for the ERs calculation is La Venta II's electricity generation.

The PDD specifies that Centro Nacional de Control de Energia (CENACE, the system operator) will be the solely provider of La Venta II's generation data. The hourly measurements of the electricity generated by La Venta II are recorded by CENACE from the ION 8500 meter located in La Venta II substation (serial number PQ-0604A002-03).


Fig.2. One line diagram and monitoring point

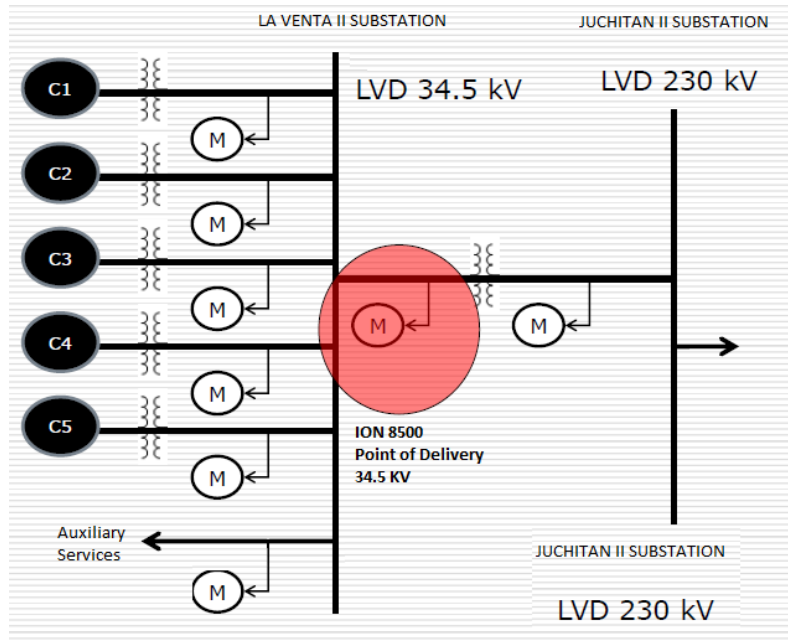

CENACE's measurement system for the electricity delivered by La Venta II is named Sistema Integral de Medicion (SIME, Integral Measurement System). This is a very reliable system that uses the communication Protocol DNP 3.0. The hourly measurements are stored in a concentrator named Concentrador de Informacion de Instalacion (CII), placed at La Venta II substation. This concentrator also sends the hourly generation information to a regional concentrator named Nodo Secundario (NS), placed in CENACE's Area de Control Oriental in Puebla (CENACE's control office for the western area of Mexico, several hundred kilometers away). Three times per day NS extracts from its local database the hourly generation of La Venta II and stores the information in a file named Hoja de Marcha. The Area de Control Oriental sends the information to CENACE headquarters in Mexico City, where it is stored in a file named Balance Diario de Energía (BD, daily balance).

In case of a transmission failure of the files to CENACE, there is a backup procedure to transfer the data in a text format. All servers at CENACE are protected through firewalls and antivirus software to prevent attacks from external sources.

Fig.3. CENACE's Measurement System (SIME)

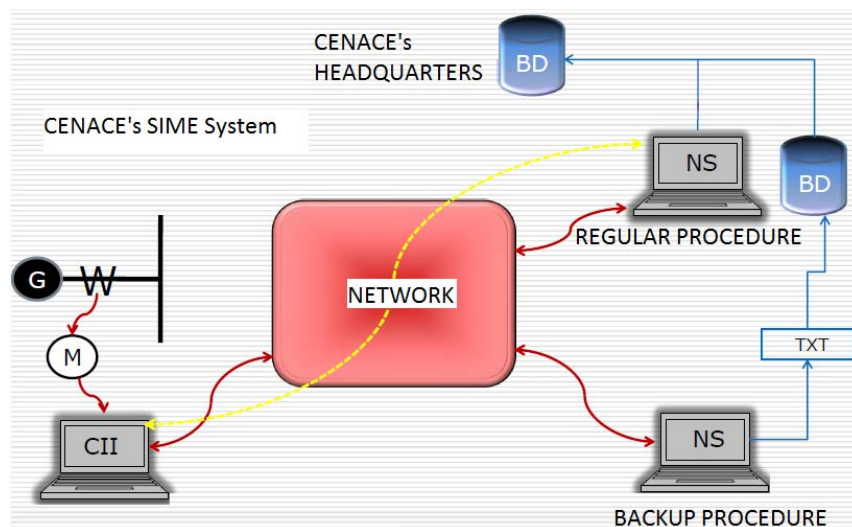

The ION 8500 meter is subjected to regular maintenance and testing regime, which includes:

- Daily monitoring by Internet, and in real time, of the power, electric tension and other variables;
- Processing per month the historical record of the generation measured by the meter;
- A monthly energy balance per installation;
- Cleaning of the meter and turning of the screws further if they needed to.

With these checks it is possible to detect any errors that the meters may be presenting.

All monitored data will be archived for at least two years after the end of the crediting period of the project.

### Data Crosschecking

According to CFE, there are no receipts of sales of the energy generated by La Venta II delivered to the next recipient of this energy: CFE Transmission Area. Thus, receipt of sales cannot be used for cross-checking of La Venta's II generation.

Instead, CFE Transmission and Generation Areas conciliate every month the energy delivered by La Venta II at the official point of delivery at 34.5 kV. This conciliation consists of an agreement for the energy delivered from Generation Area to Transmission Area. Every month, both parties sign an official internal document named "Cédula de Registro de Lecturas Mensual" that specifies the amount of delivered. This is the official document used in the cross-checking process.

### Roles and Responsibilities

As per the registered PDD, CFE has an Emissions Reduction Calculation Procedure (ERCP) with a defined organizational structure for La Venta II Project. This also includes a Quality Assurance and Control procedures in line with CDM requirements.

Fig.4. ERCP Organizational Structure

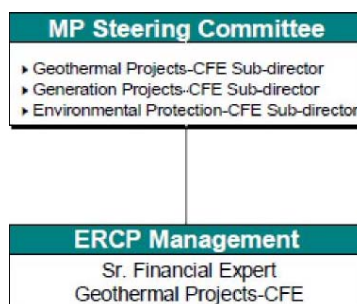


Fig.5. QA /QC procedures

Data	<ul style="list-style-type: none"> <li>▶ The project generation data.</li> <li>▶ Make coordination with CENACE to be able to implement this document.</li> <li>▶ Check calibration of electricity meters, periodically.</li> </ul>
Quality of Data Collection	<ul style="list-style-type: none"> <li>▶ Which data comes? The above</li> <li>▶ By what means does it come? By E-mail/ CD</li> <li>▶ How does it come? In Excel</li> <li>▶ How frequently does it come? Yearly</li> <li>▶ From whom does it come? From CENACE</li> <li>▶ To whom does it comes? ERCP Manager</li> </ul>
Quality of Data Processing	<ul style="list-style-type: none"> <li>▶ Original Data</li> <li>▶ Organized Data</li> <li>▶ Entered Data</li> <li>▶ Processed Data</li> <li>▶ Result</li> </ul>
Quality of Data Storage	<ul style="list-style-type: none"> <li>▶ Prevent Excel versioning problem, by keeping "a new" Excel software package.</li> <li>▶ Keep all data for 2 years after the first crediting period (9 years).</li> <li>▶ Save the ERCP file with the last date in which an alteration was made.</li> <li>▶ Keep all written documentation in a folder.</li> </ul>
Quality of Data Delivery	<ul style="list-style-type: none"> <li>▶ Provide to the verifier e-mails /CD through which the data provider (CENACE) delivered the original data</li> <li>▶ Provide to the verifier receipt of sales to final clients</li> <li>▶ Provide to the verifier all calculations made (all steps of data processing) by showing all preliminary versions of spreadsheets saved in disk</li> </ul>

Roles and responsibilities for the monitoring and reporting activities are divided among the different areas of CFE, as follows:

#### CFE Generation Area at La Venta II

- General operation of the plant.
- Preparation of the "Cédula de Registro de Lecturas Mensual".

#### CFE Transmission Area at La Venta II Substation

- Calibration and maintenance of the meters.
- Validation of the information in the "Cédula de Registro de Lecturas Mensual" (Data Cross-Checking process for the energy delivered to the grid).

#### CFE CENACE

- Operation and maintenance of SIME system.
- Measurement of the electricity delivered by La Venta II.

#### CFE Geothermal Projects Area

- Data gathering from CENACE, Generation and Transmission Areas.
- Quality control of the information provided.
- Calculation of the project GHG emission reductions.



- Data processing and preparation of the Monitoring Report.

## SECTION D. Data and parameters

### D.1. Data and parameters fixed ex ante or at renewal of crediting period

<b>Data / Parameter:</b>	EFGRID
<b>Unit:</b>	tCO <sub>2</sub> /MWh
<b>Description:</b>	Grid Emission Factor
<b>Source of data:</b>	Registered PDD
<b>Value(s) applied:</b>	0.62570
<b>Purpose of data:</b>	Baseline emissions
<b>Additional comment:</b>	N/A

### D.2. Data and parameters monitored

<b>Data / Parameter:</b>	EGy
<b>Unit:</b>	MWh
<b>Description:</b>	Electricity generation of the Project delivered to grid (net of internal consumption at La Venta II)
<b>Measured/ Calculated / Default:</b>	Measured
<b>Source of data:</b>	Measured on site at La Venta II substation and also automatically transmitted to CENACE.
<b>Value(s) of monitored parameter:</b>	279,921
<b>Monitoring equipment:</b>	Name: power meter Type: ION 8500 Accuracy Class: 0.2 Serial Number: PQ-0604A002-03 Calibration Frequency: Once a year Date of last calibration: 15/10/2013 Validity: 14/10/2014 Previous calibration: 20/11/2012 Validity: 19/11/2013
<b>Measuring/ Reading/ Recording frequency:</b>	Continuous measurement and monthly recording.
<b>Calculation method (if applicable):</b>	N/A
<b>QA/QC procedures:</b>	The metering equipment is properly calibrated and checked periodically for accuracy. To guarantee QA/QC CFE Transmission and Generation Areas conciliate every month the energy delivered by La Venta II. This cross-checking process consists of an official agreement stating the energy delivered from Generation Area to Transmission Area. Both parties sign an official internal document named "Cedula de Registro de Lecturas Mensual". The conciliation is done comparing the energy measured at La Venta II ION 85000 meter located on the 34.5kV side and the information collected by CENACE.
<b>Purpose of data:</b>	Baseline emissions
<b>Additional comment:</b>	

**D.3. Implementation of sampling plan**

N/A. The PDD does not contain a sampling plan.

**SECTION E. Calculation of emission reductions or GHG removals by sinks****E.1. Calculation of baseline emissions or baseline net GHG removals by sinks**

Baseline emissions include only CO<sub>2</sub> emissions from electricity generation in fossil fuel fired power plants that are displaced due to the project activity, calculated as follows:

Baseline emissions for the Project are calculated by using the formula:

$$BE_y = EG_y \times EF_{GRID}$$

$$= 279,921 \text{ MWh} \times 0.6257 \text{ tCO}_2\text{e/MWh} = 175,139 \text{ tCO}_2\text{e}$$

Where:

$BE_y$  = Baseline emissions in year y (tCO<sub>2</sub>/yr)

$EG_y$  = Electricity generation delivered to grid, net of internal consumptions at La Venta II (MWh)

$EF_{GRID}$  = Grid emission factor (tCO<sub>2</sub>/MWh).

**E.2. Calculation of project emissions or actual net GHG removals by sinks**

There are no project emissions ( $PE_y$ ) for the project activity as per the registered PDD.

**E.3. Calculation of leakage**

There are no leakage emissions ( $LE_y$ ) for the project activity as per the registered PDD.

**E.4. Summary of calculation of emission reductions or net anthropogenic GHG removals by sinks**

Item	Baseline emissions or baseline net GHG removals by sinks (t CO <sub>2</sub> e)	Project emissions or actual net GHG removals by sinks (t CO <sub>2</sub> e)	Leakage (t CO <sub>2</sub> e)	Emission reductions or net anthropogenic GHG removals by sinks (t CO <sub>2</sub> e)
<b>Total</b>	175,139	0	0	175,139

**E.5. Comparison of actual emission reductions or net anthropogenic GHG removals by sinks with estimates in registered PDD**

Item	Values estimated in ex-ante calculation of registered PDD	Actual values achieved during this monitoring period
Emission reductions or GHG removals by sinks (t CO <sub>2</sub> e)	289,609*	175,139

*\*The expected ERs as per the PDD has been prorated to match the duration of this monitoring period, from 1/1/1033 to 30/06/2014 (192,545 ERs + ((192,545/365) \* 181 days))*

**E.6. Remarks on difference from estimated value in registered PDD**

The total emission reductions for the period are lower than the ex-ante calculations due to lower energy productions during the monitored period. This was mainly due to the variability of the wind and the following:

- Damage suffered by the components of the wind generators
- Disconnection from the grid by the system operator (CENACE).

**E.7. Actual emission reductions or net anthropogenic GHG removals by sinks during the first commitment period and the period from 1 January 2013 onwards**

Item	Actual values achieved up to 31 December 2012	Actual values achieved from 1 January 2013 onwards
Emission reductions or GHG removals by sinks (tCO <sub>2</sub> e)	N/A	175,139

## Appendix 1. Contact information of project participants and responsible persons/ entities

<b>Project participant and/or responsible person/ entity</b>	<input checked="" type="checkbox"/> Project participant <input checked="" type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
<b>Organization name</b>	Comision Federal de Electricidad
<b>Street/P.O. Box</b>	Boulevard Adolfo Ruiz Cortines # 4156, 5th floor, Col. Jardines del Pedregal
<b>Building</b>	
<b>City</b>	Mexico DF
<b>State/Region</b>	Mexico DF
<b>Postcode</b>	01900
<b>Country</b>	Mexico
<b>Telephone</b>	(5255) 52294400 ext. 44000 or 44238.
<b>Fax</b>	
<b>E-mail</b>	
<b>Website</b>	
<b>Contact person</b>	
<b>Title</b>	Chief Executive
<b>Salutation</b>	Mr.
<b>Last name</b>	Aguinaco
<b>Middle name</b>	
<b>First name</b>	Vicente
<b>Department</b>	Environmental Protection - CFE
<b>Mobile</b>	
<b>Direct fax</b>	
<b>Direct tel.</b>	
<b>Personal e-mail</b>	

<b>Project participant and/or responsible person/ entity</b>	<input checked="" type="checkbox"/> Project participant <input checked="" type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
<b>Organization name</b>	International Bank for Reconstruction and Development (IBRD) as the Trustee of the Spanish Carbon Fund (SCF)
<b>Street/P.O. Box</b>	1818 H Street
<b>Building</b>	
<b>City</b>	Washington
<b>State/Region</b>	DC
<b>Postcode</b>	20433
<b>Country</b>	United States of America
<b>Telephone</b>	
<b>Fax</b>	
<b>E-mail</b>	
<b>Website</b>	
<b>Contact person</b>	Simon Whitehouse
<b>Title</b>	

Salutation	Mr.
Last name	Whitehouse
Middle name	
First name	Simon
Department	
Mobile	
Direct fax	
Direct tel.	
Personal e-mail	

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
Organization name	Kingdom of Spain - Ministry of Agriculture, Food and Environment and Ministry of Economy and Competitiveness
Street/P.O. Box	Alcala, 92
Building	
City	Madrid
State/Region	
Postcode	28009
Country	Spain
Telephone	
Fax	
E-mail	
Website	
Contact person	Susana Magro Andrade
Title	
Salutation	Ms.
Last name	Magro Andrade
Middle name	
First name	Susana
Department	
Mobile	
Direct fax	
Direct tel.	
Personal e-mail	

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input checked="" type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
Organization name	AZULIBER 1, S.L.
Street/P.O. Box	
Building	
City	
State/Region	
Postcode	
Country	Spain

Telephone	
Fax	
E-mail	
Website	
Contact person	Fernando Maeso
Title	
Salutation	Mr.
Last name	Maeso
Middle name	
First name	Fernando
Department	
Mobile	
Direct fax	
Direct tel.	
Personal e-mail	

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
Organization name	Comercial De Materiales De Construcción, S.L. (COMAC)
Street/P.O. Box	
Building	
City	
State/Region	
Postcode	
Country	Spain
Telephone	
Fax	
E-mail	
Website	
Contact person	Aniceto Zaragoza
Title	
Salutation	Mr.
Last name	Zaragoza
Middle name	
First name	Aniceto
Department	
Mobile	
Direct fax	
Direct tel.	
Personal e-mail	

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
Organization name	Compania Espanola De Petroleos, S.A. (CEPSA)
Street/P.O. Box	
Building	

City	
State/Region	
Postcode	
Country	Spain
Telephone	
Fax	
E-mail	
Website	
Contact person	Pedro Miro
Title	
Salutation	Mr.
Last name	Miro
Middle name	
First name	Pedro
Department	
Mobile	
Direct fax	
Direct tel.	
Personal e-mail	

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
Organization name	Endesa Generacion, S.A.
Street/P.O. Box	
Building	
City	
State/Region	
Postcode	
Country	Spain
Telephone	
Fax	
E-mail	
Website	
Contact person	David Corregidor
Title	
Salutation	Mr.
Last name	Corregidor
Middle name	
First name	David
Department	
Mobile	
Direct fax	
Direct tel.	
Personal e-mail	

<b>Project participant and/or responsible person/ entity</b>	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
<b>Organization name</b>	E.ON Generacion S.L
<b>Street/P.O. Box</b>	
<b>Building</b>	
<b>City</b>	
<b>State/Region</b>	
<b>Postcode</b>	
<b>Country</b>	Spain
<b>Telephone</b>	
<b>Fax</b>	
<b>E-mail</b>	
<b>Website</b>	
<b>Contact person</b>	Javier Anzola Perez
<b>Title</b>	
<b>Salutation</b>	Mr.
<b>Last name</b>	Anzola Perez
<b>Middle name</b>	
<b>First name</b>	Javier
<b>Department</b>	
<b>Mobile</b>	
<b>Direct fax</b>	
<b>Direct tel.</b>	
<b>Personal e-mail</b>	

<b>Project participant and/or responsible person/ entity</b>	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
<b>Organization name</b>	Gas Natural SDG, S.A
<b>Street/P.O. Box</b>	
<b>Building</b>	
<b>City</b>	
<b>State/Region</b>	
<b>Postcode</b>	
<b>Country</b>	Spain
<b>Telephone</b>	
<b>Fax</b>	
<b>E-mail</b>	
<b>Website</b>	
<b>Contact person</b>	Rosa M Sanz Garcia
<b>Title</b>	
<b>Salutation</b>	Ms
<b>Last name</b>	Sanz Garcia
<b>Middle name</b>	M
<b>First name</b>	Rosa
<b>Department</b>	
<b>Mobile</b>	



Direct fax	
Direct tel.	
Personal e-mail	

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
Organization name	Hidroelectrica Del Cantabrico, S.A.
Street/P.O. Box	
Building	
City	
State/Region	
Postcode	
Country	Spain
Telephone	
Fax	
E-mail	
Website	
Contact person	Juan Carlos Garcia Marinas
Title	
Salutation	Mr.
Last name	Garcia Marinas
Middle name	Carlos
First name	Juan
Department	
Mobile	
Direct fax	
Direct tel.	
Personal e-mail	

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
Organization name	IBERDROLA Generacion S.A.U
Street/P.O. Box	
Building	
City	
State/Region	
Postcode	
Country	Spain
Telephone	
Fax	
E-mail	
Website	
Contact person	Felix Alonso de las Fuentes
Title	

Salutation	Mr.
Last name	Alonso de las Fuentes
Middle name	
First name	Felix
Department	
Mobile	
Direct fax	
Direct tel.	
Personal e-mail	

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
Organization name	Repsol YPF S.A.
Street/P.O. Box	
Building	
City	
State/Region	
Postcode	
Country	Spain
Telephone	
Fax	
E-mail	
Website	
Contact person	Ramon Alvarez-Pedroza
Title	
Salutation	Mr.
Last name	Alvarez-Pedroza
Middle name	
First name	Ramon
Department	
Mobile	
Direct fax	
Direct tel.	
Personal e-mail	

Project participant and/or responsible person/ entity	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
Organization name	Zeroemissions Carbon Trust, S.A.
Street/P.O. Box	
Building	
City	
State/Region	
Postcode	
Country	Spain
Telephone	
Fax	

<b>E-mail</b>	
<b>Website</b>	
<b>Contact person</b>	Emilio Rodriguez-Izquierdo
<b>Title</b>	
<b>Salutation</b>	Mr.
<b>Last name</b>	Rodriguez-Izquierdo
<b>Middle name</b>	
<b>First name</b>	Emilio
<b>Department</b>	
<b>Mobile</b>	
<b>Direct fax</b>	
<b>Direct tel.</b>	
<b>Personal e-mail</b>	

<b>Project participant and/or responsible person/ entity</b>	<input checked="" type="checkbox"/> Project participant <input type="checkbox"/> Responsible person/ entity for completing the CDM-MR-FORM
<b>Organization name</b>	Cementos Portland Valderrivas S.A.
<b>Street/P.O. Box</b>	
<b>Building</b>	
<b>City</b>	
<b>State/Region</b>	
<b>Postcode</b>	
<b>Country</b>	Spain
<b>Telephone</b>	
<b>Fax</b>	
<b>E-mail</b>	
<b>Website</b>	
<b>Contact person</b>	Carlos San Felix
<b>Title</b>	
<b>Salutation</b>	Mr.
<b>Last name</b>	San Felix
<b>Middle name</b>	
<b>First name</b>	Carlos
<b>Department</b>	
<b>Mobile</b>	
<b>Direct fax</b>	
<b>Direct tel.</b>	
<b>Personal e-mail</b>	

-----

## Document information

<i>Version</i>	<i>Date</i>	<i>Description</i>
04.0	25 June 2014	Revisions to: <ul style="list-style-type: none"> <li>• Include the Attachment: Instructions for filling out the monitoring report form (these instructions supersede the "Guideline: Completing the monitoring report form" (Version 04.0));</li> <li>• Include provisions related to standardized baselines;</li> <li>• Add contact information on a responsible person(s)/entity(ies) for completing the CDM-MR-FORM in A.6 and Appendix 1;</li> <li>• Change the reference number from <i>F-CDM-MR</i> to <i>CDM-MR-FORM</i>;</li> <li>• Editorial improvement.</li> </ul>
03.2	5 November 2013	Editorial revision to correct table in page 1.
03.1	2 January 2013	Editorial revision to correct table in section E.5.
03.0	3 December 2012	Revision required to introduce a provision on reporting actual emission reductions or net anthropogenic GHG removals by sinks for the period up to 31 December 2012 and the period from 1 January 2013 onwards (EB70, Annex 11).
02.0	13 March 2012	Revision required to ensure consistency with the "Guidelines for completing the monitoring report form" (EB 66, Annex 20).
01	28 May 2010	EB 54, Annex 34. Initial adoption.
Decision Class: Regulatory Document Type: Form Business Function: Issuance Keywords: monitoring report		
